

OneHome Strategic Alignment

☰ Topics

Home Service App — Strategic, Tactical, and Operational Project Plan

Project type: Home Service Marketplace Application Team structure: 3 panels, 6 student developers Planning horizon: 1 week per tactical milestone, with daily operational tasks Primary objective: Build a functional home service application that connects customers with service providers while allowing administrators to manage the platform.

1. Strategic Plan

1.1 Project vision

Develop a working home service application that enables customers to request household services, service providers to manage and fulfill those requests, and administrators to oversee users and service operations.

The project should be designed around one fundamental transaction:

A customer requests a service → a provider accepts the request → the service is completed → the transaction is recorded.

This transaction is the project's central measure of functional success.

1.2 Strategic objectives

Strategic Objective 1

Establish a functional service marketplace

Enable customers to register, browse services, and submit service requests.

Measurable outcome: A customer can submit a valid service request and view its status.

Strategic Objective 2

Enable provider-side service fulfillment

Enable providers to manage their profiles, receive service requests, and accept or reject requests.

Measurable outcome: A provider can accept a request and update its progress.

Strategic Objective 3

Provide centralized administrative control

Enable administrators to manage users, service categories, and service requests.

Measurable outcome: An administrator can view platform records and perform authorized management actions.

Strategic Objective 4

Integrate the three panels into one application

Ensure the admin, customer, and provider modules share consistent data and workflows.

Measurable outcome: A complete service request can move from customer submission to provider acceptance and completion.

1.3 Project scope

Included in the initial version (MVP):

- User authentication and role-based access.
- Customer profiles and service request creation.
- Provider profiles and service request management.
- Service catalog and basic provider discovery.
- Booking status updates.
- Administrative management of users and service categories.
- Basic testing and project documentation.

Excluded from the initial version unless required by the instructor:

- Live GPS tracking.
- Real-time chat.
- Automated provider payouts.
- Complex recommendation algorithms.
- Advanced analytics.

- Full production-grade payment processing.

These exclusions keep the project focused on completing the core transaction rather than building peripheral features.

1.4 Team organization

The three panels are responsible for their respective interfaces and business operations. All six members share responsibility for integration, testing, and delivering a coherent application.

Panel 1 — Admin

Ballogan · Mallanes

Mission: Maintain platform integrity and administrative control.

Primary responsibilities:

- Admin login and dashboard.
- User and provider account management.
- Service category management.
- Viewing and managing service requests.
- Administrative testing and documentation.

Panel 2 — Customers

Codod · Aguiwas

Mission: Enable customers to discover and request home services.

Primary responsibilities:

- Customer registration and login interface.
- Customer profile management.
- Service catalog browsing.
- Service request creation.
- Booking status tracking and customer-side testing.

Panel 3 — Service Providers

Samdao · Lavarias

Mission: Enable providers to receive, manage, and fulfill service requests.

Primary responsibilities:

- Provider registration and profile management.
- Service offering management.
- Incoming request dashboard.
- Accepting, rejecting, and updating service requests.
- Provider-side testing and completion workflow.

1.5 Shared operating principles

1. Each panel owns its assigned module but must follow shared data structures and interface contracts.
2. Every feature must have a demonstrable working outcome.
3. Integration begins early, not after every panel finishes independently.
4. Each task must have one directly responsible owner and a verifiable deliverable.
5. No feature is considered complete until it works with the other relevant panels.

2. Tactical Objectives

The project is divided into four tactical milestones, each lasting five working days. Each milestone has a measurable outcome and a concrete deliverable.

The schedule assumes a four-week development period. Each milestone is under one week, and the daily tasks are intended to be manageable for junior developers.

Milestone overview

Week 1 Foundation and requirements

Establish the shared project structure, requirements, database schema, and interface contracts.

Deliverable: Approved requirements, working project skeleton, and agreed data model.

Week 2 Core module development

Build the customer, provider, and admin modules independently against the agreed interfaces.

Deliverable: Functional individual modules with basic CRUD operations and validation.

Week 3 Integration and end-to-end workflow

Connect the three modules and implement the complete service request lifecycle.

Deliverable: An integrated application that supports request submission, provider acceptance, and completion.

Week 4 Testing, refinement, and presentation

Test the system, fix defects, complete documentation, and prepare the demonstration.

Deliverable: Tested MVP, final documentation, and a repeatable project demonstration.

Milestone 1 — Foundation and requirements

Objective: Establish a common technical and functional foundation before parallel development begins.

Success criteria:

- All three panels agree on the minimum viable feature set.
- The shared database schema and request lifecycle are documented.
- The project repository runs on each member's development environment.
- The customer, provider, and admin roles are defined.

Milestone 2 — Core module development

Objective: Build the three modules against the shared requirements.

Success criteria:

- Customer can create a service request.
- Provider can view and respond to a request.
- Admin can view users and service records.
- Each module has basic validation and can demonstrate its primary workflow.

Milestone 3 — Integration and workflow

Objective: Connect the modules and make the main transaction work across the system.

Success criteria:

- A customer-created request appears in the provider's dashboard.
- A provider's response updates the customer's booking status.
- The administrator can view the resulting transaction.
- Booking status changes are persisted and consistent.

Milestone 4 — Testing and delivery

Objective: Verify the core workflow and prepare a stable deliverable.

Success criteria:

- The complete request-to-completion workflow passes an end-to-end test.
- Critical defects are resolved or documented.
- The project can be run from documented setup instructions.
- The final demonstration and documentation are ready.

3. Operational Directives

Operational directives translate the tactical objectives into daily tasks that each panel can execute, verify, and report.

Each day should end with a tangible output. The project manager should verify that output before the team moves to the next dependency.

Week 1 — Foundation and requirements

Tactical objective: Establish the shared architecture, requirements, and development environment.

Day	Admin — Ballogan & Mallanes	Customers — Codod & Aguiwas	Providers — Samdao & Lavarias
Day 1	Define admin functions and access rules.	Define customer journey and request fields.	Define provider journey and service offering fields.
Day 2	Document admin use cases and permissions.	Document customer use cases and screen flow.	Document provider use cases and screen flow.
Day 3	Review user, category, and request data requirements.	Define customer profile and service request data.	Define customer profile and service request data.
Day 4	Draft admin interface and shared data requirements.	Draft customer interface and request form.	Draft provider dashboard and request response interface.
Day 5	Review requirements and approve admin module scope.	Validate customer workflow and finalize screen designs.	Validate provider workflow and finalize screen designs.

Shared checkpoint: The project manager and all panels approve the requirements, data model, repository structure, and API contracts before beginning full implementation.

Required deliverables:

- Requirements and use case document.
- Database entity and relationship diagram.
- Screen wireframes.
- Shared repository and development setup instructions.

Week 2 — Core module development

Tactical objective: Build functional versions of the three modules.

Day	Admin — Ballogan & Mallanes	Customers — Codod & Aguiwas	Providers — Samdao & Lavarias
-----	-----------------------------	-----------------------------	-------------------------------

Day 1	Implement admin login and dashboard layout.	Implement customer registration and login screens.	Implement provider registration and login screens.
Day 2	Implement user listing and account management.	Implement customer profile management.	Implement provider profile and service offering management.
Day 3	Implement service category management.	Implement service catalog browsing.	Implement incoming request listing.
Day 4	Implement service request viewing and management.	Implement service request submission.	Implement accept/reject request functionality.
Day 5	Test admin operations and permissions.	Test customer request creation and validation.	Test customer request creation and validation.

Shared checkpoint: Each panel demonstrates its primary workflow independently using the agreed data structures.

Required deliverables:

- Functional admin dashboard.
- Functional customer request module.
- Functional provider request management module.
- Basic module-level test results.

Week 3 — Integration and end-to-end workflow

Tactical objective: Connect the modules through shared data and implement the complete booking lifecycle.

Day	Admin — Ballogan & Mallanes	Customers — Codod & Aguiwas	Providers — Samdao & Lavarias
Day 1	Connect admin dashboard to shared data.	Connect customer screens to request APIs.	Connect provider dashboard to request APIs.
Day 2	Verify admin can view customer and provider records.	Verify submitted requests are persisted and visible.	Verify incoming requests match customer submissions.

Day 3	Implement admin request status monitoring.	Implement booking status tracking.	Implement request acceptance and rejection updates.
Day 4	Test administrative handling of cancellations and exceptions.	Test cancellation and status updates from the customer side.	Implement service progress and completion updates.
Day 5	Verify the full transaction from the admin perspective.	Test the customer-to-provider booking workflow.	Test provider acceptance through service completion.

Shared checkpoint: Demonstrate one complete transaction:

Customer submits a request → provider receives and accepts it → provider marks the service completed → customer sees the updated status → admin can view the transaction.

Required deliverables:

- Integrated application.
- Shared data persistence.
- Working booking status transitions.
- End-to-end workflow demonstration.

Week 4 — Testing, refinement, and delivery

Tactical objective: Stabilize the MVP and prepare the final project demonstration.

Day	Admin — Ballogan & Mallanes	Customers — Codod & Aguiwas	Providers — Samdao & Lavarias
Day 1	Test admin permissions and management functions.	Test registration, request creation, and booking status.	Test provider profiles, availability, and request responses.
Day 2	Report and fix admin defects.	Report and fix customer workflow defects.	Report and fix provider workflow defects.
Day 3	Verify access restrictions and record consistency.	Test invalid inputs, duplicate	Test invalid request states and conflicting booking attempts.

		submissions, and cancellation.	
Day 4	Complete admin documentation and demonstration steps.	Complete customer documentation and demonstration steps.	Complete provider documentation and demonstration steps.
Day 5	Participate in final acceptance testing and presentation.	Participate in final acceptance testing and presentation.	Participate in final acceptance testing and presentation.

Shared checkpoint: All six members participate in a final end-to-end acceptance test and verify that the project runs using the documented setup process.

Required deliverables:

- Tested MVP.
- Defect and resolution log.
- User and technical documentation.
- Final presentation and demonstration script.

4. Task Ownership and Accountability

Each task should have one directly responsible owner, even when two people collaborate on the same module.

The following division gives each member a clear area of ownership while preserving shared responsibility for integration.

Admin panel

Ballogan

Primary focus: Admin interface, dashboard, and user management.

Mallanes

Primary focus: Service category management, request oversight, and admin testing.

Customer panel

Codod

Primary focus: Customer interface, authentication screens, and profile management.

Aguiwas

Primary focus: Service catalog, request submission, and booking status tracking.

Service provider panel

Samdao

Primary focus: Provider profile, service offerings, and incoming request dashboard.

Lavarias


Primary focus: Request acceptance, booking status transitions, and completion workflow.


These ownership assignments are proposed starting points. The team can redistribute tasks based on each member's technical strengths, but each task should retain a clearly identified owner.

5. Project Management and Alignment

5.1 Daily operating cycle

Every working day should follow a simple execution cycle:

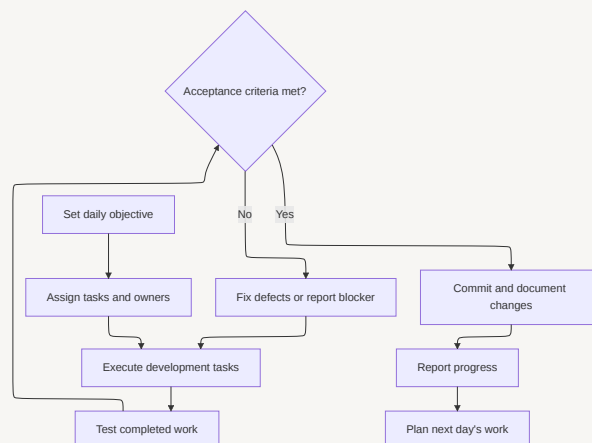

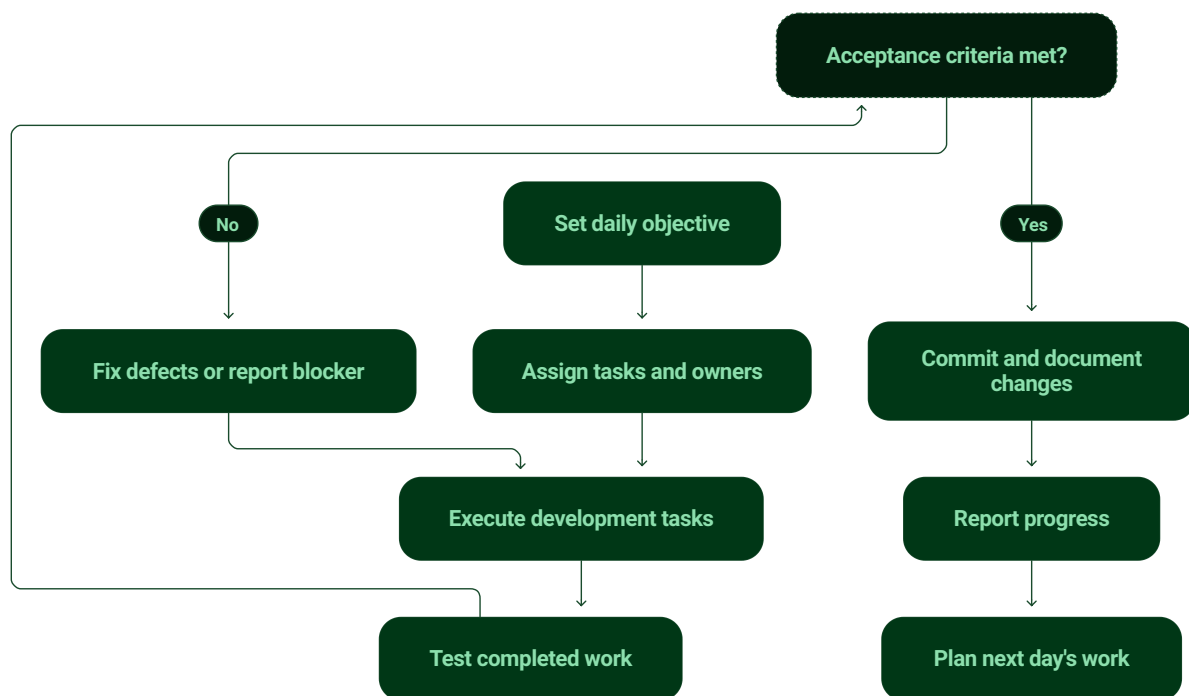

Daily reporting format

Each member reports the following:

1. **Completed:** What task was finished, and what evidence demonstrates completion?
2. **In progress:** What task is currently being worked on?
3. **Blocked:** What dependency or problem is preventing progress?
4. **Next action:** What specific task will be completed next?

This keeps reporting focused on actual progress rather than time spent working.

5.2 Definition of Done

A task is considered complete only when all applicable conditions are satisfied:

- ☐ The required functionality has been implemented.
- ☐ The feature follows the agreed data structures and business rules.
- ☐ Input validation and relevant error handling are implemented.
- ☐ The feature has been tested using at least one valid and one invalid scenario.
- ☐ The code has been committed to the shared repository.

- ☐ The responsible panel has demonstrated the feature.
- ☐ Any known limitations are documented.

A task that is merely coded but not tested should remain in progress.

5.3 Key performance indicators

The project manager should measure delivery using observable results.

KPI	Target
Tactical milestone completion	
Core workflow completion	One successful end-to-end customer-to-provider transaction.
Role functionality	All three panels can perform their defined primary use cases.
Critical defects	Zero unresolved critical defects at final acceptance.
Integration	One successful end-to-end customer-to-provider transaction.
Documentation	Setup instructions, system design, and demonstration steps are complete.

5.4 Risk management

Risk	Operational response
Panels build incompatible interfaces	Agree on API contracts and data structures in Week 1.
Features expand beyond the MVP	Prioritize the core booking workflow and defer optional features.
Integration happens too late	Begin integration during Week 2 and continue through Week 3.
Members become blocked by dependencies	Assign owners, document blockers, and resolve shared dependencies promptly.
Booking statuses become inconsistent	Define a shared state machine and validate every permitted transition.
Development environment differences cause failures	Maintain common setup instructions and test the application on multiple machines.

6. Final Strategic Alignment

The project's success depends on keeping every activity connected to the same measurable outcome.

Project Success Equation

Strategic Vision

Connect customers with qualified home service providers.

|
V

Tactical Objectives

Build the foundation, develop the modules, integrate the workflow, and validate the application.

|
V

Operational Directives

Assign daily tasks to Ballogan, Mallanes, Codod, Aguiwas, Samdao, and Lavarias.

|
V

Measurable Final Outcome

A functional, integrated, and tested home service application that successfully processes a customer request through provider acceptance and service completion.

The guiding principle: Every task must contribute to a working part of the system, every milestone must produce a verifiable deliverable, and every panel must contribute to the same end-to-end transaction.

The project is complete when the six members can demonstrate that transaction reliably—not merely when each panel has finished its own screens.
